



Department Report

Report Title: Public Works—August 2025
Name and Title: Mark Buchanan, PW Director/City Engineer

Recently Completed:

- Completion of the Mount Hope tool shed.



Ongoing:

- Park Street utilities. Lots of activity last month. The finish line is in sight.




Park Street Utility Improvements - City of Dalton - 12 Week Look Ahead Schedule Update 07/23/2025																
Strickland & Sons Pipeline, Inc.																
Task Description	6/27/2025	7/4/2025	7/11/2025	7/18/2025	7/25/2025	8/1/2025	8/8/2025	8/15/2025	8/22/2025	8/29/2025	9/5/2025	9/12/2025	9/19/2025	9/26/2025	10/3/2025	10/10/2025 % Complete
Lower Phase - Morrison Moore to Arcadia																
Layout & Staking																100%
Erosion Control																100%
Connect Sewer Laterals																100%
Install Storm Drain																100%
Install Conduit & Pull Boxes																100%
Install Curb & Driveways																100%
Install GAB																100%
Lower Phase Asphalt Base Installation							X	X								100%
Install Sidewalk							X									10%
Finish Grade & Dress up							X	X								50%
Upper Phase - Arcadia to Choice																
Clearing & Debris Removal																100%
Demo Asphalt & Debris Removal																100%
Install Waterline & Connect Services																100%
Erosion Control					X	X	X	X	X	X	X	X				70%
Layout & Staking					X	X	X	X	X	X	X	X				70%
Install Storm Drain					X	X	X	X	X	X						60%
Install Sewer & Connect Laterals						X	X	X	X	X	X					0%
Install Conduit & Pull Boxes										X	X	X	X			0%
Install GAB										X	X	X	X	X		0%
Demo Curb & Debris Removal										X	X	X				25%
Install Curb & Driveways														X	X	0%
Upper Phase Asphalt Base Installation															X	0%
Finish Paving from Morrison Moore to Choice Ave. (Entire Site)																0%
Install Sidewalk																0%
Finish Grade & Dress up															X	0%

Stop by Mark's office if you'd like to see a larger, paper version.


- Morrison Moore Pedestrian Bridge & Sidewalk.





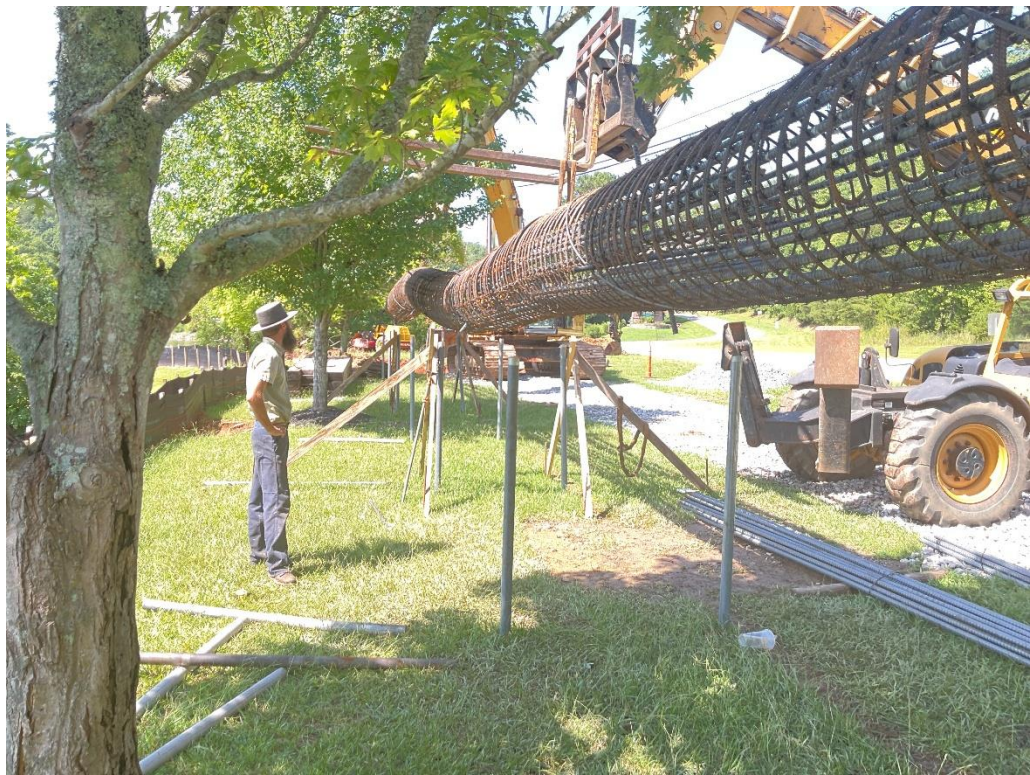



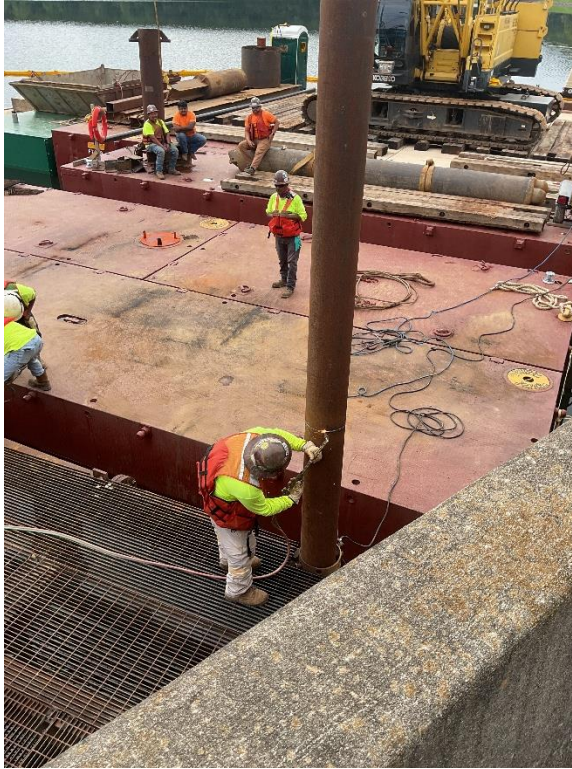









- Memorial Park Cemetery lot layout. New lots have been preliminarily laid out and await installation of plot markers by volunteers with City staff guidance. Following this, staff will work with City legal counsel to determine following steps to prepare the plots for sale and present to City Council.



- Golden Avenue storm drain. Coordination with neighboring property owners regarding necessary easements is ongoing. Georgia DOT is conducting the preliminary design of the Yahoola bridge near this location. Staff are also coordinating with them and a selected design firm to ensure a seamless transition between these two neighboring projects.
- Design and bid services for Phase 2 of the North Grove sidewalk project from Subway to Skyline Drive. Plan approved by GDOT 5/7/2025! Bids received and evaluated. A vendor selection package should be on its way to City Council in preparation for FY2026 Q1 Notice to Proceed.

Upcoming (these projects are currently either in concept, design or construction phase):

- Concrete work along Choice Street.
- Concrete work and resurfacing of Warwick Street between Park and Chestatee.
- Coordination with GDOT regarding Yahoola Bridge replacement, South Chestatee slope repair in multiple locations and the Auraria/Torrington intersection improvements.
